

Work Order ID 147579

Wednesday, June 08, 2016 2:27:41 PM

147579

Page 1

Item ID: D119-796-151 Accept ***N900040100*** Setup Start ***NS1***
 Revision ID: Stop ***NS2***
 Item Name: FWD Crosstube Installation with Step (no hardware)
 Start Date: 5/31/2016 Start Qty: 1.00 ***1*** Cust Item ID:
 Required Date: 6/24/2016 Req'd Qty: 1.00 ***1*** Customer:
 Reference:

Approvals: Process Plan: 405 Date: JUN 13 2016 Tooling: _____ Date: _____ Run Start ***NR1***
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
Draw Nbr	Revision Nbr								
D119-796-151	D								
110	Document Control	0.00							
110									
DC	Memo	0.00							
Doc.Control -USB or Paperwork	Photocopy bluefile and create labels as per PPP D119-796-151 chg 004								
120	Pick Kit	0.00							
120	Packaging								
Packaging	Memo	0.00							
Packaging									
130	Crosstubes	0.00							
130									
Crosstubes	Memo	0.11							
Crosstubes	1- Install step and clamp with the proper position per dwg D119-796-151								
	Torque all clamps to 50 IN-LBS max.								

label **DAS 21 9-89** SEP 01 2016
1
DAS 41 9-89
16-8-31
1
DAS 41 9-89
16-8-31

DQA: _____ Date: _____

**WORK ORDER NON-CONFORMANCE / UPDATE**

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER :							
Misidentified ☐	Past Due ☐								

Work Order ID 147579

Wednesday, June 08, 2016 2:27:41 PM

147579

Page 2

Item ID: D119-796-151

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: FWD Crosstube Installation with Step (no hardware)

Start Date: 5/31/2016 Start Qty: 1.00 ***1***

Cust Item ID:

Required Date: 6/24/2016 Req'd Qty: 1.00 ***1***

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
140	QC5- Inspect part completeness to step on W/O	0.00							
140									
QC	Memo	0.00							DAS 38 9-89
Quality Control	***RE-CHECK TORQUE ON CLAMP AS PER DWG.***								SEP 01 2016
	***VERIFY BY <u>147579</u> DAS 38 9-89 BATCH # TO MATCH W/O								
	***VERIFY BY <u>147579</u> DAS 38 9-89 PART # TO MATCH W/O								
150	Packaging	0.00							
150									
Packaging	Memo	0.00							DAS 41 9-89
Packaging	Identify and pack for shipping as per PPP D119-796-151								16-8-31
	<u>Au1</u>								
160	QC21- Final Inspection - Work Order Release	0.00							
160									
QC	Memo	0.02							DAS 21 9-89
Quality Control									SEP 01 2016

DAS
21
9-89
SEP 01 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
2/27/17 DC 12/10		2/27/17 DC 12/10		Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : _____					

Picklist Print

Wednesday, June 08, 2016 2:27:39 PM

Page 1

Work Order ID: 147579

147579

Parent Item: D119-796-151

D119-796-151

Parent Item Name: FWD Crosstube Installation with Step (no hardware)

Start Date: 5/31/2016

Required Date: 6/24/2016

Start Qty: 1.00

Required Qty: 1.00

Comments: IPP REV:A 14.09.09 NEW ISSUE DD VERF:JLM IPP
REV:B 14.11.19 AS PER REV.C DD VERF:JLM IPP REV:C
14.12.09 AS PER REV.PC6 DD VERF:JLM IPP REV:D 15-02-11
AS PER REV D JLM VERIFIED BY:DD

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
D119-796-141		Manufactured	No				Each	0.0000		1	DAS 41 9-89	16-8-31	
D119-796-141									**				
FWD Crosstube Installation without Step (no hardware)					148311								
D5123-3		Manufactured	No				Each	164.0000		4	DAS 41 9-89	16-5-15	
D5123-3									**				
Clamp Cushion													
					<u>Location</u>			<u>Loc Qty</u>					
					LG055			164					
					144626			56					
					145850			36					
					145851			36		4			
					146879			36					
D5149-041		Manufactured	No				Each	10.0000		2	DAS 41 9-89	16-8-31	
D5149-041									**				
Fwd Step Base Assembly					142766 142764					1			
					<u>Location</u>			<u>Loc Qty</u>					
					LG055			10					
					143466			10					
MS21920-22		Purchased	No				Each	84.0000		4	DAS 41 9-89	16-5-15	
MS21920-22									**				
Clamp													
					<u>Location</u>			<u>Loc Qty</u>					
					LG050			80					
					M133769			80		4			
					Return2016			4					
					125487			4					

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE


QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐
OTHER : _____					


ITEM	QTY	P/N	DESCRIPTION
	X	D119-796-151	XTUBE ASSY (AW119 MKII FWD)
1	1	D119-796-141	XTUBE ASSY (AW119 MKII FWD)
2	4	D5123-3	CUSHION
3	2	D5149-041	FWD STEP ASSEMBLY
4	4	MS21920-22	CLAMP

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 147579 MJS
1606-13

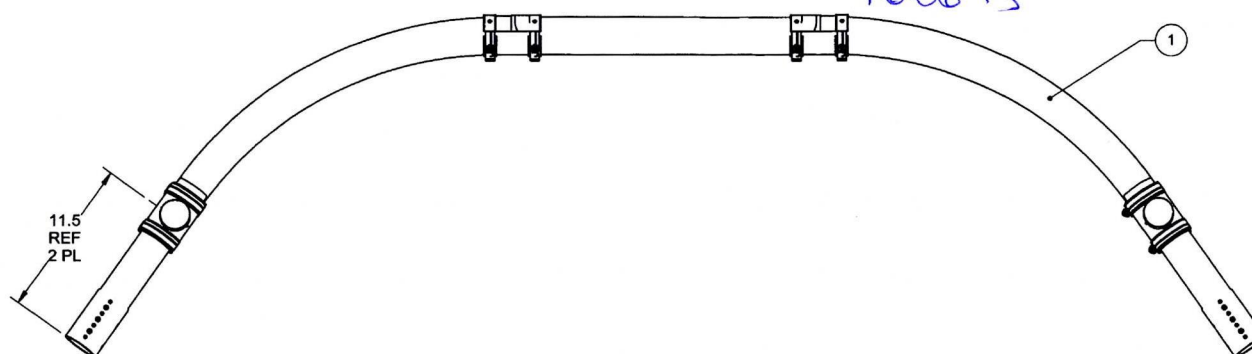

D119-796-151 XTUBE ASSY (AW119 MKII FWD)

D119-796-141 XTUBE
BENDING PLANE

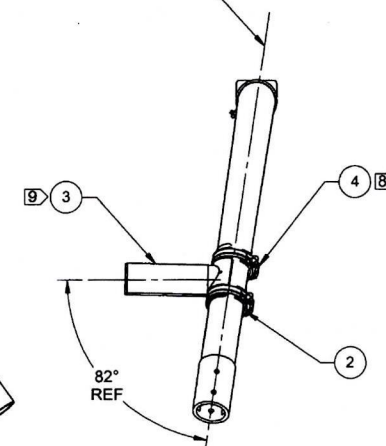

NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: IDENTIFY PER DART QSI 044 METHOD 6.5
- 7) WEIGHT: 19.87 lbs
- 8) TORQUE MS21920-22 CLAMPS TO 50 IN-LBS MAX
- 9) LOCATE STEP USING POST FITTING ON CROSSTUBE

RELEASED

2015 FEB 09

ECN 15-516 P

D	D5123-3 CLAMP CUSHION WAS D5123-9 CLAMP CUSHION, MS21920-22 WAS -24.	AP	15.01.19
C	RE-DESIGN STEP INSTALLATION	DB	14.11.24
B	D5149-043 WAS D5149-041, AN4C8A WAS AN4C10A, D2274 WAS D5153-1	AP	14.11.04
A	NEW ISSUE	AP	14.09.03
REV.	DESCRIPTION	BY	DATE
DESIGN	AP	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA DRAWING NO. D119-796-151 REV. D SHEET 1 OF 1 TITLE XTUBE ASSY (AW119 MKII FWD) NTS SCALE COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	
DRAWN	AP		
CHECKED	DB		
MFG. APPR.	JLM		
APPROVED	HS		
DE APPR.	DS		
DATE	15.01.19		

APPROVED
